



**Scottish
Water**

Trusted to serve Scotland

Taking care of your Sewer Network in Pittenweem – Project Update.

Important Scottish Water Information

We are investing in and upgrading the sewer network to help reduce sewer flooding and protect the local environment. This newsletter is to provide a further update on progress as we continue the sewer improvement works and head towards the final phases of our work in East Shore.

Update:

Our previous newsletter in May advised of a planned completion date of mid-June. Unfortunately, we have encountered some unforeseen issues regarding our remaining works which has impacted our completion date.

With regards the works along East Shore, we experienced a delay with sample results returning. This meant we were unable to progress the water main diversion as quickly as we would have liked.

The water main diversion is now complete, and we are continuing our works on the two manholes (at No18 and No5 East Shore Approx) to completion.

Work to reinstate the cobbled area around the new CSO chamber is ongoing.

The final phase of the outfall work in the outer harbour is scheduled to commence from Tuesday 18th June. As previously advised, this final section of the outfall works will be constructed by utilizing a dredging vessel located within the outer harbour.

Updated Timeline:

East Shore - The main works on East Shore are currently planned to be completed by 5th July with reinstatements/site demobilising completed by 12th July.

As this section of works are completed, we will look to reduce the working area required. This will allow us to remove some of the parking restrictions currently in place.

Outfall – The outfall works which will restart from 18th June, are planned to be completed by 1st July (weather dependant).


Following the completion of the outfall, we will then carry out some works to abandon the existing outfall pipe in The Gyles. This work will be localised and have a small working area.

General Information:

Traffic Management: The current traffic management is set up to ensure we maintain vehicle access through East Shore along to Mid and West Shore. Please help us to maintain this by adhering to the current parking restrictions that are in place.



Image: Ongoing East Shore Works

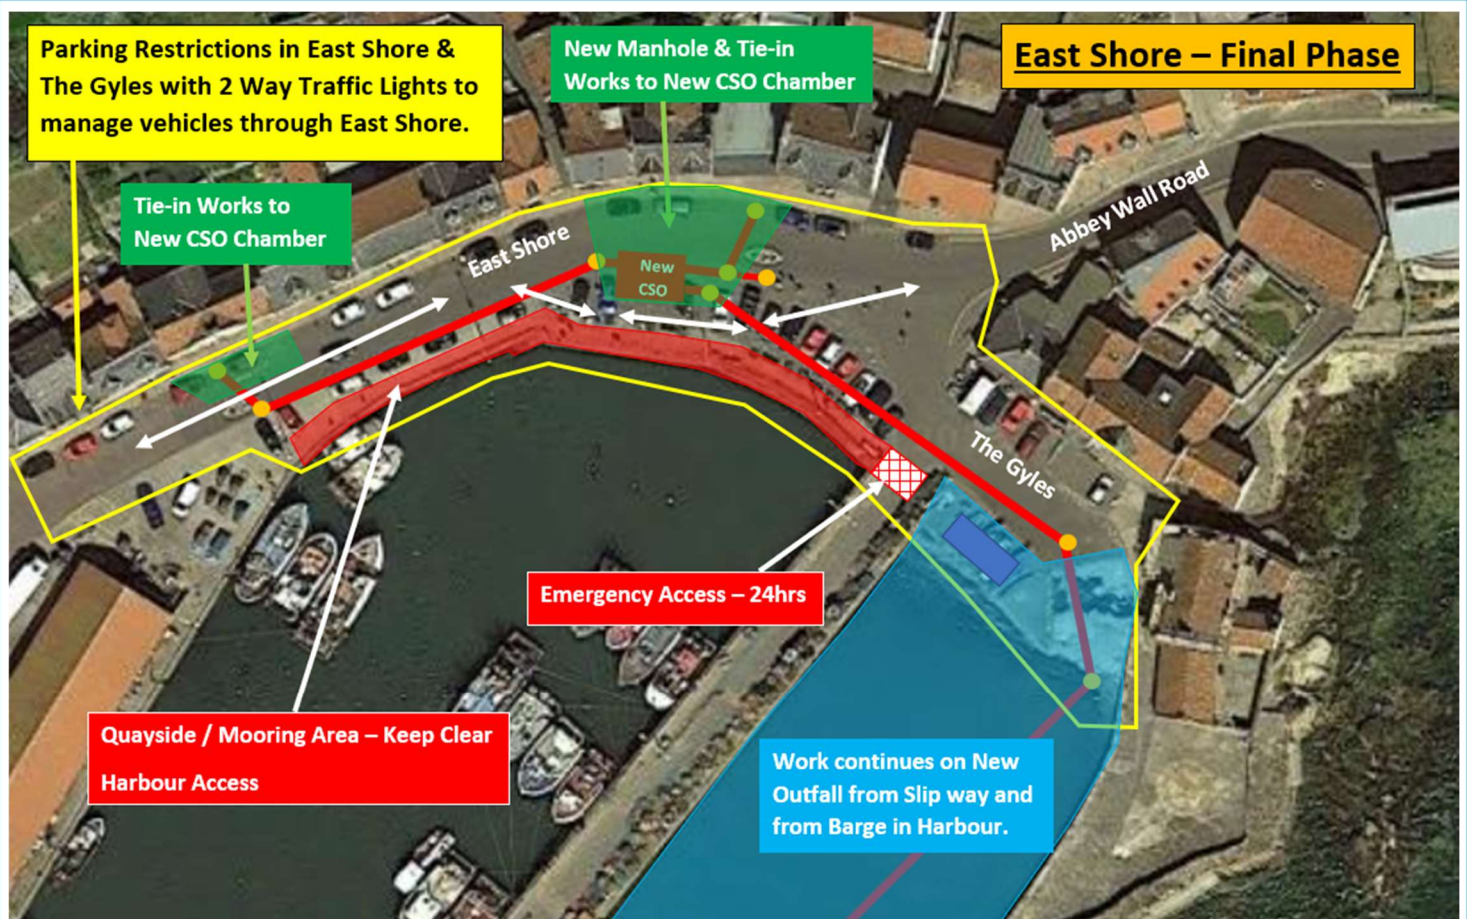

Pittenweem Arts Festival: We are committed to being clear of all our working areas well in advance of the festival and we are liaising with the arts festival organisers regards this.

The site compound beside the cemetery will also be cleared prior to the event.

Work Completion Update:

As we work towards completion we may require to work some weekends. We are working to ensure the final stages of our works are completed as soon as possible and we anticipate works to be completed and site cleared by 12th July 2024.

Project Information: Further information about our project can be found at www.scottishwater.co.uk/Pittenweem

We thank you for your continued patience, co-operation and understanding whilst we continue these essential works.

If you have any further queries, please contact Scottish Water customer helpline on 0800 0778778 quoting 'Capital/505339/CWA/Pittenweem'.

Yours Sincerely
Clive Duncan
 Customer Manager
 Caledonia Water Alliance
