ID	Task Name	Duration	Start	Finish
1	**FORRES**			
2	**Construction Phase**			
3	Start on Site	0 days	Mon 20/01/20	Mon 20/01/20
4	Site Set Up	20 days	Mon 20/01/20	Fri 14/02/20
5	New Inlet Works	161 days	Mon 17/02/20	Mon 28/09/20
6	New Sludge Storage Works	148 days	Mon 17/02/20	Wed 09/09/20
7	Biological Filter Valves Replacement	40 days	Mon 17/02/20	Fri 10/04/20
8	New MCC	48 days	Mon 17/02/20	Wed 22/04/20
9	Automatic Desludge System	66 days	Mon 17/02/20	Mon 18/05/20
10	Biological Filter Arm Refurbishment	132 days	Fri 20/03/20	Mon 21/09/20
11	Potable Water System	25 days	Mon 25/05/20	Fri 26/06/20
12	Bridge & Access Road	90 days	Thu 02/07/20	Wed 04/11/20
13	Onsite Construction Complete	0 days	Thu 05/11/20	Thu 05/11/20
14	Site Demobolise	10 days	Mon 09/11/20	Fri 20/11/20

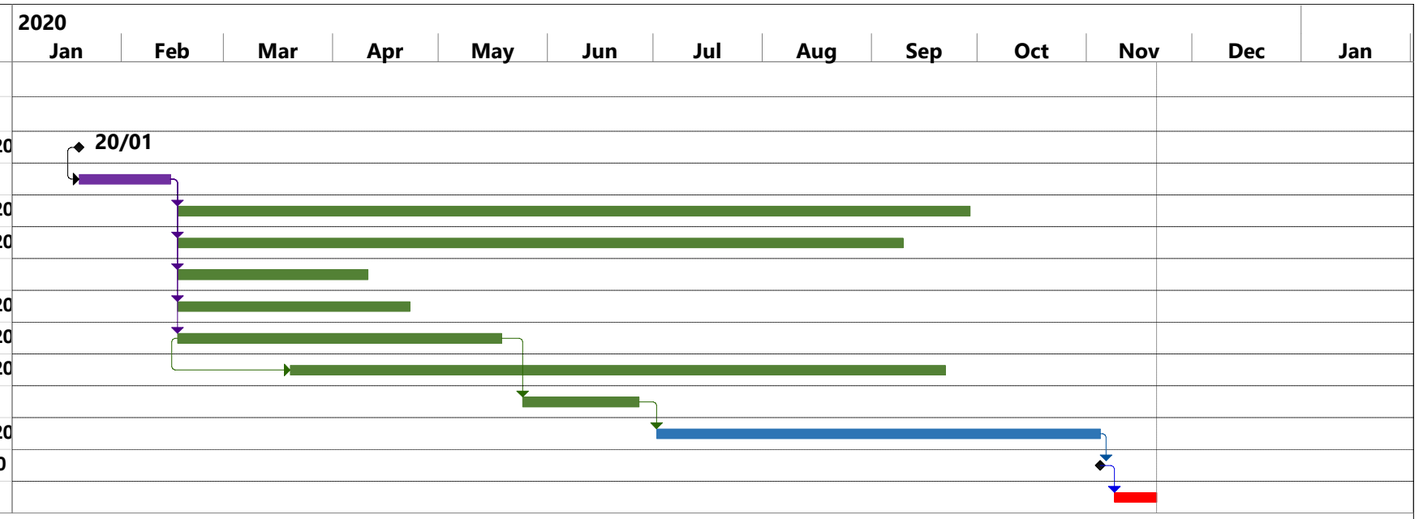

Project: Forres Construction Pro
Date: Wed 27/11/19

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
